




ID	Task Name	2008												2009											
		1st Quarter		2nd Quarter			3rd Quarter			4th Quarter				1st Quarter			2nd Quarter			3rd Quarter			4th Quarter		
		Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
11	Identify programmers to form the NCLADT	Regional Focal Points, NCEP ◆ 3/28																							
12	Set up first team meeting -- Team to meet during 6/2 week	Henry, Olsen ◆ 6/2																							
13	<b>Identify local apps to be migrated and their programmers</b>	3/1  5/7																							
14	Review NCEP local applications (AWIPS)	Olsen ◆ 3/1																							
15	Provide list of critical local apps from Survey Monkey	Olsen ◆ 3/3																							
16	Develop template for Regional Focal Points and NCEP to request local application information from MIC's/HIC's and National Centers' Directors	Tran ◆ 3/24																							
17	Submit list of local apps to be migrated to Regional Focal Points and NCEP	MIC's/HIC's, National Centers' Directors ◆ 4/30																							
18	Send Regional lists of local apps to be migrated to SEC and NCLADT with 90% of programmers identified	Regional Focal Points, NCEP ◆ 5/7																							
19	<b>Prepare for first NCLADT face-to-face meeting and TIM with Raytheon</b>	3/28  6/6																							
20	Identify a standalone machine to run AWIPS II	NCLADT ◆ 4/1																							
21	Install TO-8 (S/W delivered to sites - 3/27/08)	NCLADT ◆ 4/4																							
22	Conduct AWIPS II training exercises to prepare NCLADT for TIM with Raytheon	3/28  Olsen 4/23																							

Project: Local-App-Migration-Road Ma Date: Mon 4/7/08	Task		Milestone	◆	External Tasks	
	Split		Summary		External Milestone	◆
	Progress		Project Summary		Deadline	





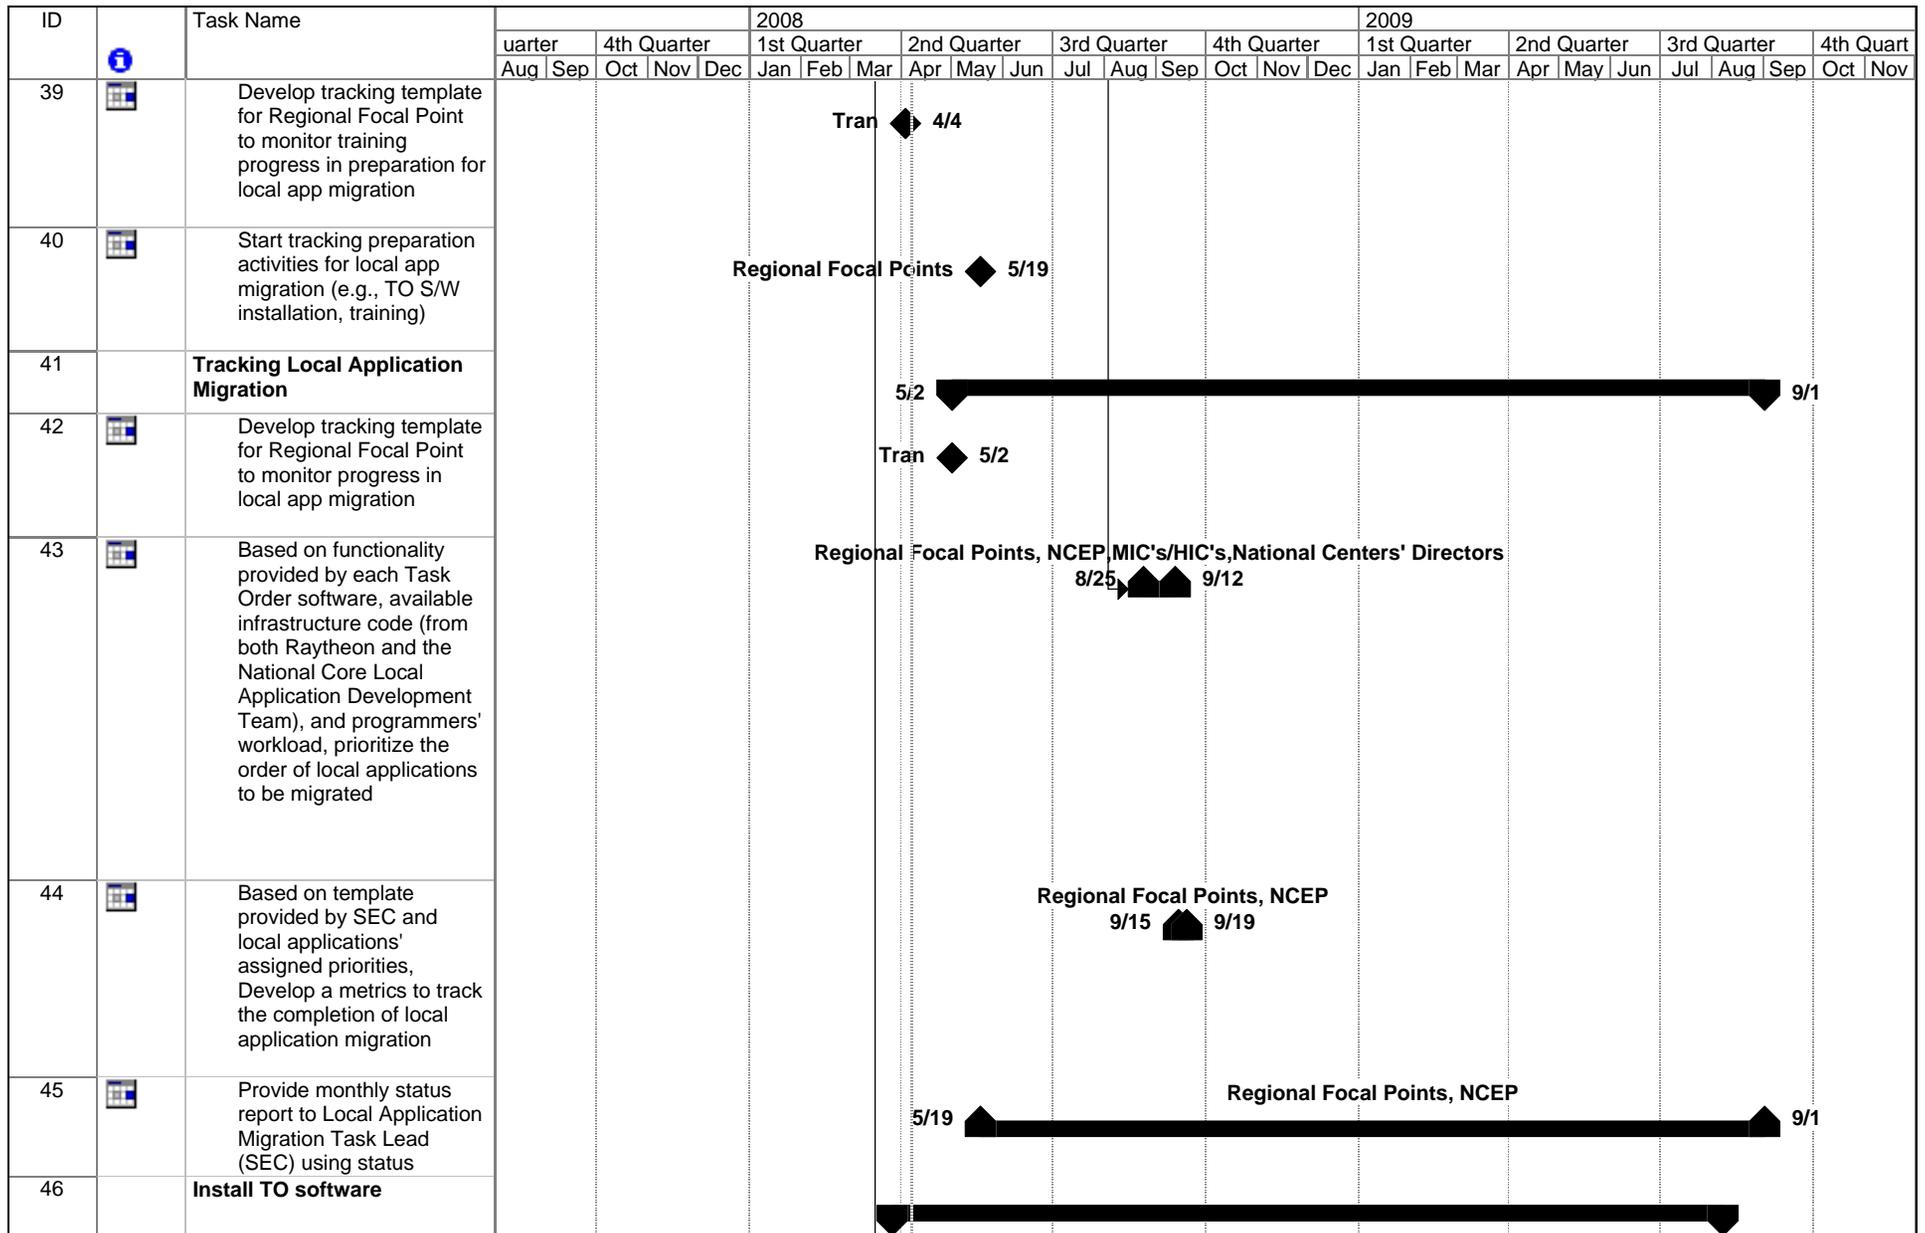

Project: Local-App-Migration-Road Ma  
Date: Mon 4/7/08

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



ID	Task Name	2008												2009																
		3rd Quarter		4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter		
		Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	
63	Migrate or Interface Local Applications (including large applications migrated by NCLADT)	<b>NCLADT, Local App Developers</b> 																												
64	Loading data into new localization database	<b>Local App Developers</b> ◆ 4/30																												
65	Procedure to XML bundle migration	<b>Resources TBD</b> 																												
66	Convert WarnGen Templates to AWIPS II Format	<b>Resources TBD</b> 																												
67	Certify that all critical local applications assigned to their sites are addressed and adhere to NCLADT guidelines	<b>MIC's/HIC's,National Centers' Directors</b> ◆ 9/1																												

Project: Local-App-Migration-Road Ma Date: Mon 4/7/08	Task		Milestone	◆	External Tasks	
	Split		Summary		External Milestone	◆
	Progress		Project Summary		Deadline	↓
