ID	Task Name	Start	Finish
1	**Distributed Modeling System (DMS) 1.0: Basic DMS Functionality**	**Mon 3/24/03**	**Fri 1/16/04**
2	**DMS 1.0 - Project planning**	**Mon 3/24/03**	**Tue 5/27/03**
3	**Initial planning**	**Mon 3/24/03**	**Thu 4/10/03**
11	**Discovery session at ABRFC**	**Fri 4/11/03**	**Fri 5/2/03**
15	**Detailed planning**	**Thu 4/17/03**	**Thu 5/22/03**
26	**RFC #2 Planning**	**Thu 4/17/03**	**Tue 5/27/03**
28	**DMS 1.0 - Requirements**	**Tue 4/22/03**	**Wed 6/18/03**
29	**Data Management Track**	**Tue 4/22/03**	**Fri 5/16/03**
35	**User Interfaces for prototype**	**Mon 5/5/03**	**Tue 5/20/03**
38	**Tools Implementation Track**	**Mon 4/28/03**	**Wed 5/28/03**
43	**Requirements review**	**Wed 5/28/03**	**Wed 6/18/03**
49	**DMS 1.0 - Implementation**	**Wed 6/18/03**	**Fri 9/26/03**
50	**Data Management**	**Wed 6/18/03**	**Tue 9/2/03**
54	**User Interfaces for prototype**	**Mon 6/30/03**	**Tue 9/2/03**
58	**Tools**	**Wed 6/18/03**	**Wed 9/3/03**
63	**Documentation**	**Wed 6/18/03**	**Fri 9/12/03**
68	System and Integration Testing	Wed 9/3/03	Wed 9/24/03
69	Present implementation progress to OHD leadership	Wed 9/24/03	Thu 9/25/03
70	DMS 1.0 Deployed at RFC #1	Thu 9/25/03	Fri 9/26/03
71	**DMS 1.0 - Testing**	**Fri 9/26/03**	**Tue 12/16/03**
72	**RFC #1 Testing**	**Fri 9/26/03**	**Tue 12/16/03**
78	**RFC #2 Testing**	**Mon 10/6/03**	**Thu 11/27/03**
85	**Present progress**	**Mon 10/6/03**	**Mon 12/1/03**
89	**DMS 1.0 - Summary**	**Tue 12/16/03**	**Fri 1/16/04**
90	DMS 1.0 - Detailed Review	Tue 12/16/03	Tue 12/23/03
91	Compile Test Results during a meeting at OHD in Silver Spring or conference call	Tue 12/23/03	Thu 12/25/03
92	Present DMS 1.0 progress and results to OHD leadership	Thu 12/25/03	Fri 12/26/03
93	Create document summarizing project for all RFCs	Fri 12/26/03	Fri 1/16/04

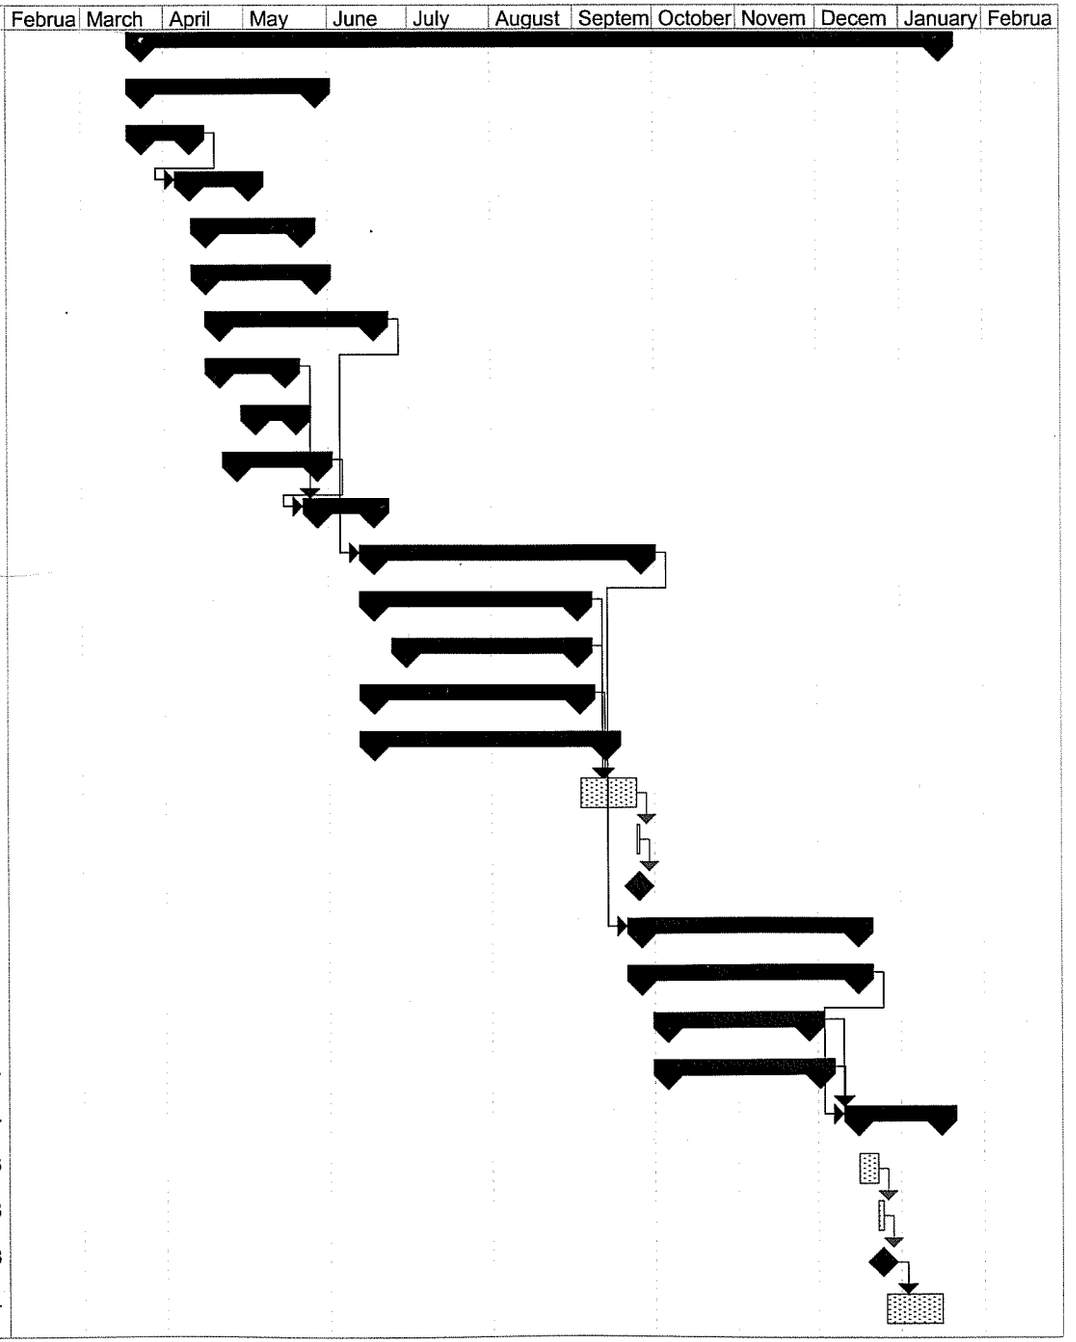

DMS 1.0 Project Schedule
